

Mbarara Integrated Concrete Products Factory

Investor, Engineering, Financial & Expansion Master Report 2026-2035

Prepared as a consolidated master report from the latest web platform modules: Financial Simulator, Inventory, Production Planning, Quality Control and Laboratory, ERP, Competitor and Market Intelligence, PostgreSQL structure, Product Costing, and Risk Register.

Currency: UGX only. Data confidence labels are preserved throughout. Market prices, contacts, competitor records, machinery costs, and supplier terms must be re-verified before investment decisions.

Report file	Mbarara_Integrated_Concrete_Factory_Master_Report.pdf
Planning horizon	2026-2035
Location	Mbarara, Uganda
Starter budget	UGX 130,000,000
Phase 1 essential startup cost	UGX 128,000,000
Budget buffer	UGX 2,000,000
Data status	Estimated / Quotation Required / Needs verification unless explicitly marked Verified

Table of Contents

Table of Contents	2
1. Executive Summary	3
2. Market Analysis	4
3. Competitor Analysis	4
4. Product Portfolio	5
5. Product Mix Ratios	5
6. Raw Material Consumption	6
7. Machinery Analysis	7
8. Factory Layout Summary	7
9. Utility Consumption	7
10. Laboratory and Quality Control	7
11. Legal and Regulatory Roadmap	8
12. Financial Model	8
13. ERP Integration Summary	8
14. Market Gap Analysis	9
15. Risk Register	9
16. Implementation Roadmap 2026-2035	10
17. East African Expansion Strategy	10
18. Appendices	10

1. Executive Summary

The proposed Mbarara Integrated Concrete Products Factory is now planned as a lean Phase 1 concrete products factory serving Mbarara City and Western Uganda within a strict UGX 130,000,000 starter budget. The immediate product set is limited to hollow blocks, solid blocks, standard pavers, and limited kerbstones.

Ready-mix concrete, culverts, drainage channels, decorative/specialist pavers, owned delivery trucks, heavy lifting equipment, and extra production lines are deliberately deferred until verified orders and cash flow can fund them.

The current integrated model shows monthly revenue of UGX 140,020,000, gross profit of UGX 50,192,578, and net profit of UGX 36,092,578. The UGX 20,000,000 monthly profit target is reached under the seed assumptions.

Starter budget ceiling	UGX 130,000,000
Phase 1 essential startup cost	UGX 128,000,000
Budget buffer	UGX 2,000,000
Budget feasibility status	Feasible within UGX 130,000,000 starter budget
Monthly revenue	UGX 140,020,000
Monthly production/material cost	UGX 89,827,422
Monthly expenses	UGX 14,100,000
Gross profit	UGX 50,192,578
Net profit	UGX 36,092,578
Break-even revenue	UGX 39,334,142
ROI estimate	338.4%
UGX 20,000,000 target	Reached


UGX 130M Phase 1 Budget Feasibility

The launch plan avoids buying a full-scale factory on day one. It funds only the essential line needed to start producing saleable blocks, standard pavers, and kerbstones while keeping a small cash buffer.

Semi-automatic block/paver machine, mixer, vibrator	UGX 45,000,000	Essential quotation required
Starter moulds: 6-inch, 8-inch, solid, 60 mm, 80 mm, kerbstone	UGX 14,000,000	Essential only
Site preparation, curing yard, drainage, basic shed works	UGX 14,000,000	Lean starter works
Electrical and water connection setup	UGX 7,000,000	Essential utilities
Pallets, wheelbarrows, hand tools, racks, safety gear	UGX 8,000,000	Starter handling
Starter raw materials and packaging	UGX 24,000,000	Working stock
Permits, basic laboratory tools, compliance and safety	UGX 4,000,000	Basic QC only
Launch labour, security, administration	UGX 7,000,000	Opening month reserve
Sales, local transport, customer visits	UGX 3,000,000	Launch campaign
Unallocated cash buffer	UGX 2,000,000	Do not spend unless necessary
Ready-mix concrete batching plant and transit mixers	Add after verified orders, positive cash flow, and written supplier quotations.	
Culvert production line and heavy lifting equipment	Add after verified orders, positive cash flow, and written supplier quotations.	
Drainage channel mould expansion	Add after verified orders, positive cash flow, and written supplier quotations.	
Grass/permeable and cobblestone paver moulds	Add after verified orders, positive cash flow, and written supplier quotations.	
Dedicated delivery truck purchase	Add after verified orders, positive cash flow, and written supplier quotations.	
Advanced laboratory equipment beyond basic batch control	Add after verified orders, positive cash flow, and written supplier quotations.	

Second production line and regional depots	Add after verified orders, positive cash flow, and written supplier quotations.

Monthly Profit Projection

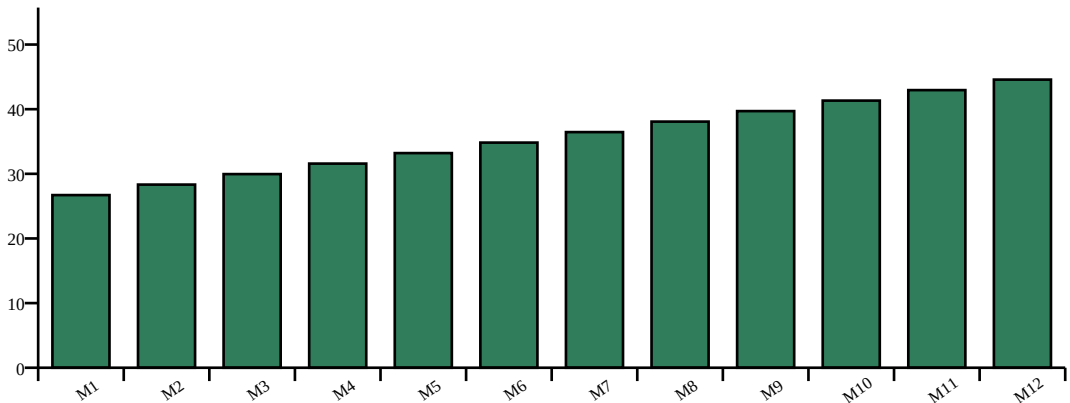

2. Market Analysis

The first sales campaign should focus on areas with active housing, commercial construction, schools, roadworks, fuel stations, hotels, NGOs, churches, and hardware distribution. Customer demand records below are planning estimates and require field verification.


Target Western Uganda focus areas					
Mbarara City, Rwampara, Isingiro, Ntungamo, Bushenyi, Ibanda, Kiruhura, Sheema, Lyantonde, Kabale, Rukungiri					
Mbarara Heights Estate	property developers	Mbarara City	6-inch blocks, 8-inch blocks, 60 mm pavers	28,000	medium
Nyamitanga Hardware	hardware stores	Mbarara City	4-inch blocks, 6-inch blocks, 60 mm pavers	14,000	medium
Western Roads JV	government projects	Mbarara City and regional roads	kerbstones, drainage channels, culverts, 80 mm pavers	5,000	medium
Lake View Schools	schools	Ruti	8-inch blocks, 60 mm pavers, drainage channels	4,200	high
Western Fuel Station Group	fuel stations	Mbarara, Ntungamo, Bushenyi	80 mm pavers, kerbstones, drainage channels	3,600	medium

3. Competitor Analysis

Competitor records are seeded for investigation only. No competitor record should be treated as verified until supported by website evidence, Facebook page review, phone call, quotation, field visit, marketplace check, or government record.

iConic Concrete	Mbarara City	precast supplier	hollow blocks, pavers, precast products	medium	Needs verification
Master Industries	Mbarara City	paver maker	pavers, blocks	medium	Needs verification
Stone Providers Ltd	Rwampara	quarry supplier	stone dust, aggregates	medium	Needs verification
Nicomah	Mbarara City	small block yard	hollow blocks	medium	Needs verification
BIMS Bloks Mbarara	Mbarara City	small block yard	hollow blocks, solid blocks	high	Needs verification
local block yards in Mbarara	Mbarara City	small block yard	4-inch, 6-inch, 8-inch hollow blocks	high	Needs verification
local quarry suppliers around Western Uganda	Western Uganda	quarry supplier	stone dust, aggregates	medium	Needs verification

Hima Cement distributors	Mbarara City	cement distributor	cement	medium	Needs verification
Tororo Cement distributors	Mbarara City	cement distributor	cement	medium	Needs verification
Kampala Cement distributors	Mbarara City	cement distributor	cement	medium	Needs verification
Simba Cement distributors	Mbarara City	cement distributor	cement	medium	Needs verification

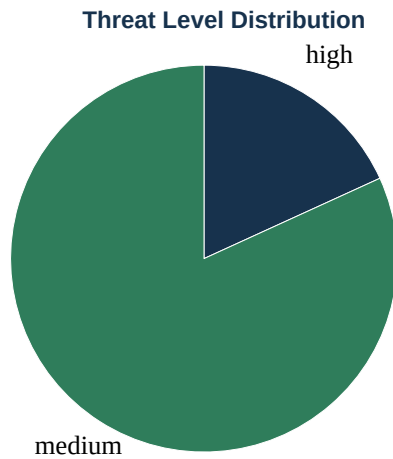

4. Product Portfolio

4-inch hollow blocks	blocks	piece	250	UGX 1,800	Estimated
6-inch hollow blocks	blocks	piece	1,000	UGX 2,600	Estimated
8-inch hollow blocks	blocks	piece	650	UGX 3,400	Estimated
solid blocks	blocks	piece	300	UGX 3,000	Estimated
60 mm pavers	pavers	piece	850	UGX 2,400	Quotation Required
80 mm pavers	pavers	piece	450	UGX 3,200	Quotation Required
grass/permeable pavers	pavers	piece	0	UGX 4,200	Quotation Required
cobblestone pavers	pavers	piece	0	UGX 2,100	Estimated
kerbstones	precast	piece	60	UGX 18,000	Estimated
drainage channels	precast	piece	0	UGX 55,000	Quotation Required
culverts	precast	piece	0	UGX 180,000	Quotation Required
ready-mix concrete	ready-mix	m3	0	UGX 410,000	Quotation Required

5. Product Mix Ratios

4-inch hollow blocks	1 cement : 6 stone dust	Assumption: validate through batch trials, curing records, and compression tests.
6-inch hollow blocks	1 cement : 7 stone dust	Assumption: validate through batch trials, curing records, and compression tests.
8-inch hollow blocks	1 cement : 6 stone dust	Assumption: validate through batch trials, curing records, and compression tests.
solid blocks	1 cement : 5 stone dust : 1 sand	Assumption: validate through batch trials, curing records, and compression tests.


60 mm pavers	1 cement : 3 sand : 3 aggregate	Assumption: validate through batch trials, curing records, and compression tests.
80 mm pavers	1 cement : 2.5 sand : 3 aggregate	Assumption: validate through batch trials, curing records, and compression tests.
grass/permeable pavers	1 cement : 3 sand : 3 aggregate	Assumption: validate through batch trials, curing records, and compression tests.
cobblestone pavers	1 cement : 3 sand : 3 aggregate	Assumption: validate through batch trials, curing records, and compression tests.
kerbstones	1 cement : 2 sand : 3 aggregate	Assumption: validate through batch trials, curing records, and compression tests.
drainage channels	1 cement : 2 sand : 3 aggregate	Assumption: validate through batch trials, curing records, and compression tests.
culverts	1 cement : 2 sand : 3 aggregate with reinforcement where specified	Assumption: validate through batch trials, curing records, and compression tests.
ready-mix concrete	Design mix by strength class	Assumption: validate through batch trials, curing records, and compression tests.

6. Raw Material Consumption

Inventory is linked to production batches and financial costing. Reorder levels are planning values and should be adjusted after at least one month of measured usage.

cement bags	646.0	bags	UGX 21,964,000	19.0	220.0	Hima Cement distributors
stone dust tonnes	126.0	tonnes	UGX 5,670,000	15.8	35.0	local quarry suppliers around Western Uganda
sand tonnes	45.0	tonnes	UGX 1,710,000	12.9	18.0	local quarry suppliers around Western Uganda
aggregates tonnes	51.0	tonnes	UGX 3,060,000	12.8	22.0	local quarry suppliers around Western Uganda
diesel litres	250.0	litres	UGX 1,400,000	13.9	120.0	Mbarara diesel supplier
water m3	112.0	m3	UGX 470,400	14.0	55.0	local quarry suppliers around Western Uganda
pallets	160.0	units	UGX 5,600,000	53.3	60.0	local pallet supplier
moulds	12.0	units	UGX 9,000,000	Non-consumable	4.0	machine/mould supplier
spare parts	25.0	units	UGX 3,125,000	Non-consumable	10.0	machine spares supplier

Inventory Stock Value (UGX million)

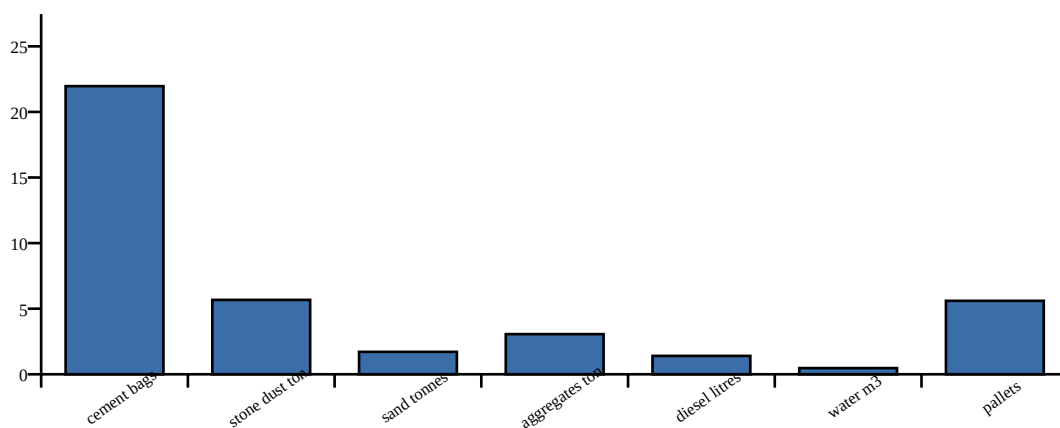

7. Machinery Analysis

Semi-automatic block/paver machine with mixer and vibrator	Blocks, 60 mm pavers, 80 mm pavers	Essential Phase 1 production line sized for the UGX 130M budget.	Quotation Required
Starter mould set	6-inch, 8-inch, solid blocks, standard pavers, kerbstones	Buy only the moulds needed for the first sales campaign.	Quotation Required
Additional specialist moulds	Grass pavers, cobblestones, drainage channels, culverts	Deferred until demand is proven and cash flow supports mould expansion.	Quotation Required
Batching plant and transit mixers	Ready-mix concrete	Phase 3 expansion after core products generate repeatable profit.	Quotation Required

8. Factory Layout Summary

The recommended layout separates inbound materials, cement storage, batching/mixing, forming, curing yards, finished goods dispatch, laboratory, administration, spare parts store, and vehicle circulation. Final layout requires land survey, drainage design, and local authority approval.

Raw materials yard	Stone dust, sand, aggregates	Allow truck turning, drainage, and stockpile separation.
Covered cement store	Cement bags	Keep dry, secure, and close to batching.
Production bay	Mixing and forming	Minimize material handling and protect machines.
Curing yard	Curing and batch traceability	Track curing start date and batch ID.
QC laboratory	Tests and certificates	Keep records linked to production batches.
Dispatch zone	Customer loading	Separate from inbound quarry deliveries.


9. Utility Consumption

Electricity	UGX 780 per kWh	Machine hours, mixer load, lighting	Estimated
Water	UGX 4,200 per m3	Mixing, curing, cleaning	Estimated
Diesel	UGX 5,600 per litre	Loader, forklift, delivery, backup power	Estimated

10. Laboratory and Quality Control

The QC module tracks each batch by batch ID, date, product, operator, material use, mix ratio, curing start date, curing age, compressive strength, water absorption, density, dimensions, visual defects, and approval status.

BATCH-2026-001	6-inch hollow blocks	5.8 MPa	8.2%	1,720 kg/m3	Pass	2	Passed
BATCH-2026-002	80 mm pavers	36.0 MPa	5.1%	2,180 kg/m3	Pass	1	Passed
BATCH-2026-003	kerbstones	24.0 MPa	6.5%	2,290 kg/m3	Fail	5	Hold

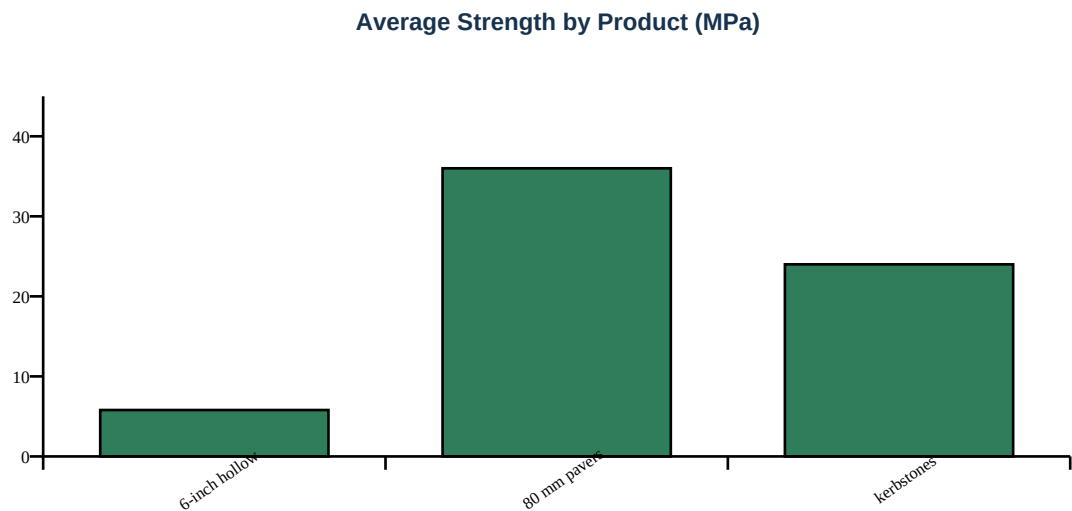

11. Legal and Regulatory Roadmap

Mbarara City authority	Planning, building, trade, and local approvals	Pre-construction
NEMA	Environmental screening and mitigation	Pre-construction
Occupational safety office	Worker safety compliance and inspections	Before commissioning
URA	Tax registration, invoicing, and compliance	Before trading
UNBS / standards review	Product standards and certification pathway	Before making certification claims
Water and electricity utilities	Service connections and metering	Pre-commissioning

12. Financial Model

4-inch hollow blocks	UGX 1,722	UGX 1,493	UGX 138	UGX 92	UGX 1,800	UGX 78	4.3%	Estimate
6-inch hollow blocks	UGX 1,722	UGX 1,493	UGX 138	UGX 92	UGX 2,600	UGX 878	33.8%	Estimate
8-inch hollow blocks	UGX 2,164	UGX 1,935	UGX 138	UGX 92	UGX 3,400	UGX 1,236	36.3%	Estimate
solid blocks	UGX 2,441	UGX 2,212	UGX 138	UGX 92	UGX 3,000	UGX 559	18.6%	Estimate
60 mm pavers	UGX 2,036	UGX 1,796	UGX 148	UGX 92	UGX 2,400	UGX 364	15.2%	Quotation Required
80 mm pavers	UGX 2,308	UGX 2,068	UGX 148	UGX 92	UGX 3,200	UGX 892	27.9%	Quotation Required
grass/permeable pavers	UGX 2,036	UGX 1,796	UGX 148	UGX 92	UGX 4,200	UGX 2,164	51.5%	Quotation Required
cobblestone pavers	UGX 2,036	UGX 1,796	UGX 148	UGX 92	UGX 2,100	UGX 64	3.0%	Estimate
kerbstones	UGX 8,891	UGX 8,300	UGX 499	UGX 92	UGX 18,000	UGX 9,109	50.6%	Estimate
drainage channels	UGX 23,603	UGX 22,000	UGX 1,511	UGX 92	UGX 55,000	UGX 31,397	57.1%	Quotation Required
culverts	UGX 80,932	UGX 76,580	UGX 4,260	UGX 92	UGX 180,000	UGX 99,068	55.0%	Quotation Required
ready-mix concrete	UGX 351,964	UGX 334,400	UGX 17,472	UGX 92	UGX 410,000	UGX 58,036	14.2%	Quotation Required


13. ERP Integration Summary

Sales	Customers, products, unit price, delivery, paid amount	Daily sales, balances, gross revenue
Inventory	Items, suppliers, add stock, issue stock, reorder levels	Stock value, low-stock alerts, usage reports
Production	Batches, operators, material consumption, rejected products	Efficiency and batch traceability
Quality Control	Batch-linked laboratory tests	Pass/fail status, rejection rate, certificates
Expenses	Payroll, utilities, maintenance, transport	Monthly profit and supplier balances

14. Market Gap Analysis

1	6-inch hollow blocks	9	7	6	3	9	14
2	8-inch hollow blocks	8	6	7	3	8	14
3	60 mm pavers	8	5	7	4	8	14
4	80 mm pavers	7	5	8	4	8	14
5	kerbstones	6	4	8	5	8	13
6	drainage channels	6	3	8	6	8	13
7	ready-mix concrete	5	4	8	8	9	10
8	culverts	5	3	8	8	7	9
9	grass/permeable pavers	4	3	7	5	6	9
10	cobblestone pavers	5	4	6	4	6	9
11	solid blocks	5	6	5	3	5	6
12	4-inch hollow blocks	6	7	4	3	5	5

Opportunity Score by Product

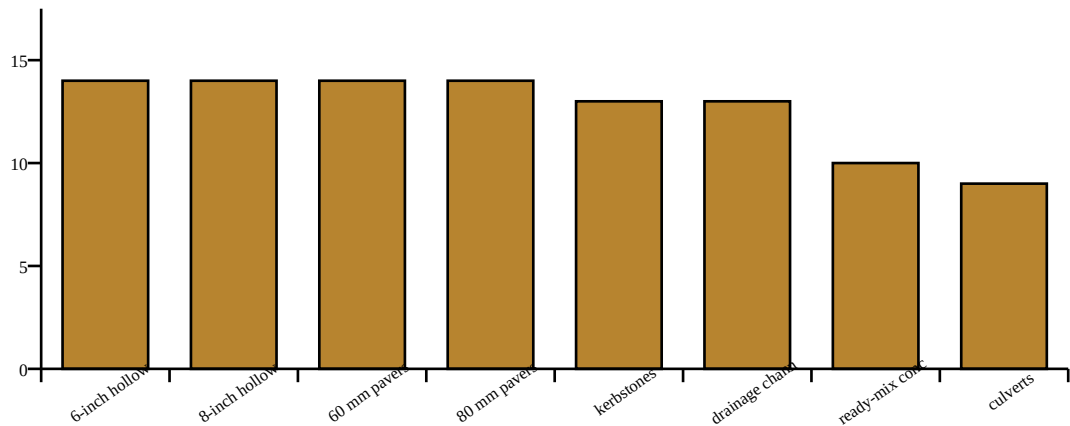

15. Risk Register

UGX 130,000,000 starter budget is tight and can fail if equipment quotations rise above allowance.	Financial	High	High	Buy only essential Phase 1 equipment, keep a UGX 2,000,000 cash buffer, and require written quotations before deposits.
Market prices are unverified and may differ by district and delivery distance.	Market	High	High	Run weekly field price checks before final investment decisions.
Cement price volatility reduces margins.	Supply	Medium	High	Negotiate distributor credit terms and maintain supplier alternatives.

Insufficient curing and QC discipline leads to rejected blocks.	Quality	Medium	High	Enforce curing registers, batch traceability, and compression testing.
Equipment downtime disrupts monthly profit target.	Operations	Medium	High	Keep critical spares, preventive maintenance, and backup mixer capacity.
Delayed customer payments strain working capital.	Financial	Medium	Medium	Use customer credit limits and require deposits for delivery-heavy orders.
Permit or environmental compliance delay.	Regulatory	Low	High	Sequence NEMA, city authority, water, and occupational safety actions early.
Expanding into ready-mix, culverts, or heavy precast too early consumes working capital.	Financial	Medium	High	Defer non-essential products until Phase 1 has repeat customers, positive cash flow, and verified equipment quotations.

16. Implementation Roadmap 2026-2035

2026	Launch within UGX 130,000,000 using essential machine, starter moulds, basic site works, starter stock, permits, QC tools, and local sales.
2027	Stabilize blocks, standard pavers, and kerbstones; formalize QC records and target Mbarara City and Rwampara.
2028	Add extra moulds only from retained earnings; test drainage channel demand through quotations before buying moulds.
2029	Scale mould sets and secure framework supply agreements.
2030	Evaluate ready-mix feasibility and transit mixer economics only after verified demand and strong cash reserves.
2031	Expand to Ntungamo, Bushenyi, Ibanda, Kiruhura, Sheema, and Lyantonde.
2032	Build regional stockist network and contractor credit scoring.
2033	Add advanced precast products where municipal demand is verified.
2034	Prepare East African partnerships and logistics corridors.
2035	Evaluate second factory or satellite yard based on verified profitability.

17. East African Expansion Strategy

Expansion should follow proof of quality, repeatable monthly profit, and working-capital discipline in Western Uganda. The recommended path is distribution-led before asset-heavy regional production expansion.

Western Uganda consolidation	Shortest delivery routes and strongest relationships	Focus on Mbarara City, Rwampara, Isingiro, Ntungamo, Bushenyi, Ibanda, Kiruhura, Sheema, Lyantonde, Kabale, and Rukungiri.
Border market testing	Contractor and NGO demand may justify selective shipments	Use quotation-based sales before fixed depots.
Regional partnerships	Lower capex than immediate new factories	Partner with hardware stores and contractors first.
Second production base	Only after verified monthly profit and demand density	Trigger by multi-year contracts and reliable raw material supply.

18. Appendices

Data Confidence Labels

Verified	Confirmed by reliable documentation, invoice, field check, or quotation.
Estimated	Planning value based on current model assumptions and prior project context.
Quotation Required	Do not use for procurement or investment until a supplier quotation is obtained.
Needs verification	Seed record requiring field visit, phone check, website check, or documentary proof.

Table	Description
Assumption	Model input that must be validated by quotations, lab tests, or site-specific engineering.

PostgreSQL Integration Tables

Table	Description
products	Product portfolio, pricing, mix ratios, and active status.
suppliers	Cement, quarry, diesel, water, spares, and logistics suppliers.
customers	Demand, buying power, payment reliability, and target products.
production_batches	Material consumption, rejected products, curing, and machine hours.
inventory	Stock master data, unit costs, reorder levels, and daily consumption.
sales	Customer sales, unit price, delivery cost, paid amount, and balances.
expenses	Operating costs and supplier/payee balances.
quality_tests	Batch-linked strength, absorption, density, dimensions, defects, and approval.
competitor_records	Future market-intelligence extension with source tracking.

Investment Disclaimer

This master report is a planning document. It is not a substitute for engineering design, statutory approvals, audited financial statements, tax advice, legal advice, environmental approval, or binding supplier/customer quotations. Market prices, competitor details, contacts, GPS data, capacity estimates, and machinery costs must be re-verified before investment decisions.

Appendix Product Sheet 1: 4-inch hollow blocks

4-inch hollow blocks is classified as Phase 1 active. The current planning unit is piece, the planned selling price is UGX 1,800, and the daily Phase 1 volume is 250. Confidence remains Estimated; quotations and laboratory trials must be completed before final procurement or sales commitments.

Mix assumption: 1 cement : 6 stone dust. For Phase 1, production should be batch-controlled, cured by date, and linked to quality certificates before delivery to contractors or hardware stores.

Product category	blocks
Phase status	Phase 1 active
Sales priority	Do not stock heavily before confirmed orders
Estimated unit cost	UGX 1,722
Estimated unit margin	UGX 78
Opportunity score	5
Budget note	No additional non-essential moulds should be purchased until cash flow supports them.

Appendix Product Sheet 2: 6-inch hollow blocks

6-inch hollow blocks is classified as Phase 1 active. The current planning unit is piece, the planned selling price is UGX 2,600, and the daily Phase 1 volume is 1,000. Confidence remains Estimated; quotations and laboratory trials must be completed before final procurement or sales commitments.

Mix assumption: 1 cement : 7 stone dust. For Phase 1, production should be batch-controlled, cured by date, and linked to quality certificates before delivery to contractors or hardware stores.

Product category	blocks
Phase status	Phase 1 active
Sales priority	First campaign
Estimated unit cost	UGX 1,722
Estimated unit margin	UGX 878
Opportunity score	14
Budget note	No additional non-essential moulds should be purchased until cash flow supports them.

Appendix Product Sheet 3: 8-inch hollow blocks

8-inch hollow blocks is classified as Phase 1 active. The current planning unit is piece, the planned selling price is UGX 3,400, and the daily Phase 1 volume is 650. Confidence remains Estimated; quotations and laboratory trials must be completed before final procurement or sales commitments.

Mix assumption: 1 cement : 6 stone dust. For Phase 1, production should be batch-controlled, cured by date, and linked to quality certificates before delivery to contractors or hardware stores.

Product category	blocks
Phase status	Phase 1 active
Sales priority	First campaign
Estimated unit cost	UGX 2,164
Estimated unit margin	UGX 1,236
Opportunity score	14
Budget note	No additional non-essential moulds should be purchased until cash flow supports them.

Appendix Product Sheet 4: solid blocks

solid blocks is classified as Phase 1 active. The current planning unit is piece, the planned selling price is UGX 3,000, and the daily Phase 1 volume is 300. Confidence remains Estimated; quotations and laboratory trials must be completed before final procurement or sales commitments.

Mix assumption: 1 cement : 5 stone dust : 1 sand. For Phase 1, production should be batch-controlled, cured by date, and linked to quality certificates before delivery to contractors or hardware stores.

Product category	blocks
Phase status	Phase 1 active
Sales priority	Do not stock heavily before confirmed orders
Estimated unit cost	UGX 2,441
Estimated unit margin	UGX 559
Opportunity score	6
Budget note	No additional non-essential moulds should be purchased until cash flow supports them.

Appendix Product Sheet 5: 60 mm pavers

60 mm pavers is classified as Phase 1 active. The current planning unit is piece, the planned selling price is UGX 2,400, and the daily Phase 1 volume is 850. Confidence remains Quotation Required; quotations and laboratory trials must be completed before final procurement or sales commitments.

Mix assumption: 1 cement : 3 sand : 3 aggregate. For Phase 1, production should be batch-controlled, cured by date, and linked to quality certificates before delivery to contractors or hardware stores.

Product category	pavers
Phase status	Phase 1 active
Sales priority	First campaign
Estimated unit cost	UGX 2,036
Estimated unit margin	UGX 364
Opportunity score	14
Budget note	No additional non-essential moulds should be purchased until cash flow supports them.

Appendix Product Sheet 6: 80 mm pavers

80 mm pavers is classified as Phase 1 active. The current planning unit is piece, the planned selling price is UGX 3,200, and the daily Phase 1 volume is 450. Confidence remains Quotation Required; quotations and laboratory trials must be completed before final procurement or sales commitments.

Mix assumption: 1 cement : 2.5 sand : 3 aggregate. For Phase 1, production should be batch-controlled, cured by date, and linked to quality certificates before delivery to contractors or hardware stores.

Product category	pavers
Phase status	Phase 1 active
Sales priority	First campaign
Estimated unit cost	UGX 2,308
Estimated unit margin	UGX 892
Opportunity score	14
Budget note	No additional non-essential moulds should be purchased until cash flow supports them.

Appendix Product Sheet 7: grass/permeable pavers

grass/permeable pavers is classified as Deferred expansion item. The current planning unit is piece, the planned selling price is UGX 4,200, and the daily Phase 1 volume is 0. Confidence remains Quotation Required; quotations and laboratory trials must be completed before final procurement or sales commitments.

Mix assumption: 1 cement : 3 sand : 3 aggregate. For Phase 1, production should be batch-controlled, cured by date, and linked to quality certificates before delivery to contractors or hardware stores.

Product category	pavers
Phase status	Deferred expansion item
Sales priority	Do not stock heavily before confirmed orders
Estimated unit cost	UGX 2,036
Estimated unit margin	UGX 2,164
Opportunity score	9
Budget note	No additional non-essential moulds should be purchased until cash flow supports them.

Appendix Product Sheet 8: cobblestone pavers

cobblestone pavers is classified as Deferred expansion item. The current planning unit is piece, the planned selling price is UGX 2,100, and the daily Phase 1 volume is 0. Confidence remains Estimated; quotations and laboratory trials must be completed before final procurement or sales commitments.

Mix assumption: 1 cement : 3 sand : 3 aggregate. For Phase 1, production should be batch-controlled, cured by date, and linked to quality certificates before delivery to contractors or hardware stores.

Product category	pavers
Phase status	Deferred expansion item
Sales priority	Do not stock heavily before confirmed orders
Estimated unit cost	UGX 2,036
Estimated unit margin	UGX 64
Opportunity score	9
Budget note	No additional non-essential moulds should be purchased until cash flow supports them.

Appendix Product Sheet 9: kerbstones

kerbstones is classified as Phase 1 active. The current planning unit is piece, the planned selling price is UGX 18,000, and the daily Phase 1 volume is 60. Confidence remains Estimated; quotations and laboratory trials must be completed before final procurement or sales commitments.

Mix assumption: 1 cement : 2 sand : 3 aggregate. For Phase 1, production should be batch-controlled, cured by date, and linked to quality certificates before delivery to contractors or hardware stores.

Product category	precast
Phase status	Phase 1 active
Sales priority	First campaign
Estimated unit cost	UGX 8,891
Estimated unit margin	UGX 9,109
Opportunity score	13
Budget note	No additional non-essential moulds should be purchased until cash flow supports them.

Appendix Product Sheet 10: drainage channels

drainage channels is classified as Deferred expansion item. The current planning unit is piece, the planned selling price is UGX 55,000, and the daily Phase 1 volume is 0. Confidence remains Quotation Required; quotations and laboratory trials must be completed before final procurement or sales commitments.

Mix assumption: 1 cement : 2 sand : 3 aggregate. For Phase 1, production should be batch-controlled, cured by date, and linked to quality certificates before delivery to contractors or hardware stores.

Product category	precast
Phase status	Deferred expansion item
Sales priority	Do not stock heavily before confirmed orders
Estimated unit cost	UGX 23,603
Estimated unit margin	UGX 31,397
Opportunity score	13
Budget note	No additional non-essential moulds should be purchased until cash flow supports them.

Appendix Product Sheet 11: culverts

culverts is classified as Deferred expansion item. The current planning unit is piece, the planned selling price is UGX 180,000, and the daily Phase 1 volume is 0. Confidence remains Quotation Required; quotations and laboratory trials must be completed before final procurement or sales commitments.

Mix assumption: 1 cement : 2 sand : 3 aggregate with reinforcement where specified. For Phase 1, production should be batch-controlled, cured by date, and linked to quality certificates before delivery to contractors or hardware stores.

Product category	precast
Phase status	Deferred expansion item
Sales priority	Do not stock heavily before confirmed orders
Estimated unit cost	UGX 80,932
Estimated unit margin	UGX 99,068
Opportunity score	9
Budget note	No additional non-essential moulds should be purchased until cash flow supports them.

Appendix Product Sheet 12: ready-mix concrete

ready-mix concrete is classified as Deferred expansion item. The current planning unit is m3, the planned selling price is UGX 410,000, and the daily Phase 1 volume is 0. Confidence remains Quotation Required; quotations and laboratory trials must be completed before final procurement or sales commitments.

Mix assumption: Design mix by strength class. For Phase 1, production should be batch-controlled, cured by date, and linked to quality certificates before delivery to contractors or hardware stores.

Product category	ready-mix
Phase status	Deferred expansion item
Sales priority	Do not stock heavily before confirmed orders
Estimated unit cost	UGX 351,964
Estimated unit margin	UGX 58,036
Opportunity score	10
Budget note	No additional non-essential moulds should be purchased until cash flow supports them.

Appendix Monthly Forecast 1: Jan 2026

This monthly forecast page extends the integrated model through Jan 2026. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Phase 1 stabilization
Estimated revenue	UGX 86,812,400
Estimated production/material cost	UGX 55,693,002
Estimated operating expenses	UGX 14,100,000
Estimated net profit	UGX 17,019,398
Profit target status	Below UGX 20,000,000
Management focus	Verify quotations and protect the UGX 2,000,000 buffer.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 2: Feb 2026

This monthly forecast page extends the integrated model through Feb 2026. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Phase 1 stabilization
Estimated revenue	UGX 88,352,620
Estimated production/material cost	UGX 56,681,103
Estimated operating expenses	UGX 14,149,350
Estimated net profit	UGX 17,522,167
Profit target status	Below UGX 20,000,000
Management focus	Prioritize 6-inch blocks and 8-inch blocks for contractors.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 3: Mar 2026

This monthly forecast page extends the integrated model through Mar 2026. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Phase 1 stabilization
Estimated revenue	UGX 89,892,840
Estimated production/material cost	UGX 57,669,205
Estimated operating expenses	UGX 14,198,700
Estimated net profit	UGX 18,024,935
Profit target status	Below UGX 20,000,000
Management focus	Push 60 mm pavers through schools, homes, and hardware stores.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 4: Apr 2026

This monthly forecast page extends the integrated model through Apr 2026. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Phase 1 stabilization
Estimated revenue	UGX 91,433,060
Estimated production/material cost	UGX 58,657,307
Estimated operating expenses	UGX 14,248,050
Estimated net profit	UGX 18,527,703
Profit target status	Below UGX 20,000,000
Management focus	Use kerbstones only for confirmed contractor orders.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 5: May 2026

This monthly forecast page extends the integrated model through May 2026. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Phase 1 stabilization
Estimated revenue	UGX 92,973,280
Estimated production/material cost	UGX 59,645,408
Estimated operating expenses	UGX 14,297,400
Estimated net profit	UGX 19,030,472
Profit target status	Below UGX 20,000,000
Management focus	Improve curing discipline and reduce rejects.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 6: Jun 2026

This monthly forecast page extends the integrated model through Jun 2026. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Phase 1 stabilization
Estimated revenue	UGX 94,513,500
Estimated production/material cost	UGX 60,633,510
Estimated operating expenses	UGX 14,346,750
Estimated net profit	UGX 19,533,240
Profit target status	Below UGX 20,000,000
Management focus	Collect customer balances before expanding stock.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 7: Jul 2026

This monthly forecast page extends the integrated model through Jul 2026. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Phase 1 stabilization
Estimated revenue	UGX 96,053,720
Estimated production/material cost	UGX 61,621,612
Estimated operating expenses	UGX 14,396,100
Estimated net profit	UGX 20,036,008
Profit target status	Above UGX 20,000,000
Management focus	Negotiate cement distributor terms.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 8: Aug 2026

This monthly forecast page extends the integrated model through Aug 2026. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Phase 1 stabilization
Estimated revenue	UGX 97,593,940
Estimated production/material cost	UGX 62,609,713
Estimated operating expenses	UGX 14,445,450
Estimated net profit	UGX 20,538,777
Profit target status	Above UGX 20,000,000
Management focus	Test one new district sales route without buying extra machinery.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 9: Sep 2026

This monthly forecast page extends the integrated model through Sep 2026. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Phase 1 stabilization
Estimated revenue	UGX 99,134,160
Estimated production/material cost	UGX 63,597,815
Estimated operating expenses	UGX 14,494,800
Estimated net profit	UGX 21,041,545
Profit target status	Above UGX 20,000,000
Management focus	Review price changes and update the simulator.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 10: Oct 2026

This monthly forecast page extends the integrated model through Oct 2026. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Phase 1 stabilization
Estimated revenue	UGX 100,674,380
Estimated production/material cost	UGX 64,585,917
Estimated operating expenses	UGX 14,544,150
Estimated net profit	UGX 21,544,313
Profit target status	Above UGX 20,000,000
Management focus	Reserve cash for maintenance and pallets.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 11: Nov 2026

This monthly forecast page extends the integrated model through Nov 2026. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Phase 1 stabilization
Estimated revenue	UGX 102,214,600
Estimated production/material cost	UGX 65,574,018
Estimated operating expenses	UGX 14,593,500
Estimated net profit	UGX 22,047,082
Profit target status	Above UGX 20,000,000
Management focus	Prepare quotations for deferred products without committing deposits.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 12: Dec 2026

This monthly forecast page extends the integrated model through Dec 2026. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Phase 1 stabilization
Estimated revenue	UGX 103,754,820
Estimated production/material cost	UGX 66,562,120
Estimated operating expenses	UGX 14,642,850
Estimated net profit	UGX 22,549,850
Profit target status	Above UGX 20,000,000
Management focus	Close the month with inventory count and QC summary.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 13: Jan 2027

This monthly forecast page extends the integrated model through Jan 2027. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Phase 1 stabilization
Estimated revenue	UGX 105,295,040
Estimated production/material cost	UGX 67,550,222
Estimated operating expenses	UGX 14,692,200
Estimated net profit	UGX 23,052,618
Profit target status	Above UGX 20,000,000
Management focus	Verify quotations and protect the UGX 2,000,000 buffer.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 14: Feb 2027

This monthly forecast page extends the integrated model through Feb 2027. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Phase 1 stabilization
Estimated revenue	UGX 106,835,260
Estimated production/material cost	UGX 68,538,323
Estimated operating expenses	UGX 14,741,550
Estimated net profit	UGX 23,555,387
Profit target status	Above UGX 20,000,000
Management focus	Prioritize 6-inch blocks and 8-inch blocks for contractors.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 15: Mar 2027

This monthly forecast page extends the integrated model through Mar 2027. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Phase 1 stabilization
Estimated revenue	UGX 108,375,480
Estimated production/material cost	UGX 69,526,425
Estimated operating expenses	UGX 14,790,900
Estimated net profit	UGX 24,058,155
Profit target status	Above UGX 20,000,000
Management focus	Push 60 mm pavers through schools, homes, and hardware stores.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 16: Apr 2027

This monthly forecast page extends the integrated model through Apr 2027. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Phase 1 stabilization
Estimated revenue	UGX 109,915,700
Estimated production/material cost	UGX 70,514,527
Estimated operating expenses	UGX 14,840,250
Estimated net profit	UGX 24,560,923
Profit target status	Above UGX 20,000,000
Management focus	Use kerbstones only for confirmed contractor orders.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 17: May 2027

This monthly forecast page extends the integrated model through May 2027. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Phase 1 stabilization
Estimated revenue	UGX 111,455,920
Estimated production/material cost	UGX 71,502,628
Estimated operating expenses	UGX 14,889,600
Estimated net profit	UGX 25,063,692
Profit target status	Above UGX 20,000,000
Management focus	Improve curing discipline and reduce rejects.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 18: Jun 2027

This monthly forecast page extends the integrated model through Jun 2027. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Phase 1 stabilization
Estimated revenue	UGX 112,996,140
Estimated production/material cost	UGX 72,490,730
Estimated operating expenses	UGX 14,938,950
Estimated net profit	UGX 25,566,460
Profit target status	Above UGX 20,000,000
Management focus	Collect customer balances before expanding stock.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 19: Jul 2027

This monthly forecast page extends the integrated model through Jul 2027. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Phase 1 stabilization
Estimated revenue	UGX 114,536,360
Estimated production/material cost	UGX 73,478,831
Estimated operating expenses	UGX 14,988,300
Estimated net profit	UGX 26,069,229
Profit target status	Above UGX 20,000,000
Management focus	Negotiate cement distributor terms.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 20: Aug 2027

This monthly forecast page extends the integrated model through Aug 2027. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Phase 1 stabilization
Estimated revenue	UGX 116,076,580
Estimated production/material cost	UGX 74,466,933
Estimated operating expenses	UGX 15,037,650
Estimated net profit	UGX 26,571,997
Profit target status	Above UGX 20,000,000
Management focus	Test one new district sales route without buying extra machinery.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 21: Sep 2027

This monthly forecast page extends the integrated model through Sep 2027. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Phase 1 stabilization
Estimated revenue	UGX 117,616,800
Estimated production/material cost	UGX 75,455,035
Estimated operating expenses	UGX 15,087,000
Estimated net profit	UGX 27,074,765
Profit target status	Above UGX 20,000,000
Management focus	Review price changes and update the simulator.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 22: Oct 2027

This monthly forecast page extends the integrated model through Oct 2027. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Phase 1 stabilization
Estimated revenue	UGX 119,157,020
Estimated production/material cost	UGX 76,443,136
Estimated operating expenses	UGX 15,136,350
Estimated net profit	UGX 27,577,534
Profit target status	Above UGX 20,000,000
Management focus	Reserve cash for maintenance and pallets.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 23: Nov 2027

This monthly forecast page extends the integrated model through Nov 2027. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Phase 1 stabilization
Estimated revenue	UGX 120,697,240
Estimated production/material cost	UGX 77,431,238
Estimated operating expenses	UGX 15,185,700
Estimated net profit	UGX 28,080,302
Profit target status	Above UGX 20,000,000
Management focus	Prepare quotations for deferred products without committing deposits.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 24: Dec 2027

This monthly forecast page extends the integrated model through Dec 2027. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Phase 1 stabilization
Estimated revenue	UGX 122,237,460
Estimated production/material cost	UGX 78,419,340
Estimated operating expenses	UGX 15,235,050
Estimated net profit	UGX 28,583,070
Profit target status	Above UGX 20,000,000
Management focus	Close the month with inventory count and QC summary.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 25: Jan 2028

This monthly forecast page extends the integrated model through Jan 2028. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Retained-earnings expansion
Estimated revenue	UGX 123,777,680
Estimated production/material cost	UGX 79,407,441
Estimated operating expenses	UGX 15,284,400
Estimated net profit	UGX 29,085,839
Profit target status	Above UGX 20,000,000
Management focus	Verify quotations and protect the UGX 2,000,000 buffer.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 26: Feb 2028

This monthly forecast page extends the integrated model through Feb 2028. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Retained-earnings expansion
Estimated revenue	UGX 125,317,900
Estimated production/material cost	UGX 80,395,543
Estimated operating expenses	UGX 15,333,750
Estimated net profit	UGX 29,588,607
Profit target status	Above UGX 20,000,000
Management focus	Prioritize 6-inch blocks and 8-inch blocks for contractors.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 27: Mar 2028

This monthly forecast page extends the integrated model through Mar 2028. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Retained-earnings expansion
Estimated revenue	UGX 126,858,120
Estimated production/material cost	UGX 81,383,645
Estimated operating expenses	UGX 15,383,100
Estimated net profit	UGX 30,091,375
Profit target status	Above UGX 20,000,000
Management focus	Push 60 mm pavers through schools, homes, and hardware stores.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 28: Apr 2028

This monthly forecast page extends the integrated model through Apr 2028. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Retained-earnings expansion
Estimated revenue	UGX 128,398,340
Estimated production/material cost	UGX 82,371,746
Estimated operating expenses	UGX 15,432,450
Estimated net profit	UGX 30,594,144
Profit target status	Above UGX 20,000,000
Management focus	Use kerbstones only for confirmed contractor orders.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 29: May 2028

This monthly forecast page extends the integrated model through May 2028. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Retained-earnings expansion
Estimated revenue	UGX 129,938,560
Estimated production/material cost	UGX 83,359,848
Estimated operating expenses	UGX 15,481,800
Estimated net profit	UGX 31,096,912
Profit target status	Above UGX 20,000,000
Management focus	Improve curing discipline and reduce rejects.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 30: Jun 2028

This monthly forecast page extends the integrated model through Jun 2028. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Retained-earnings expansion
Estimated revenue	UGX 131,478,780
Estimated production/material cost	UGX 84,347,950
Estimated operating expenses	UGX 15,531,150
Estimated net profit	UGX 31,599,680
Profit target status	Above UGX 20,000,000
Management focus	Collect customer balances before expanding stock.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 31: Jul 2028

This monthly forecast page extends the integrated model through Jul 2028. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Retained-earnings expansion
Estimated revenue	UGX 133,019,000
Estimated production/material cost	UGX 85,336,051
Estimated operating expenses	UGX 15,580,500
Estimated net profit	UGX 32,102,449
Profit target status	Above UGX 20,000,000
Management focus	Negotiate cement distributor terms.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 32: Aug 2028

This monthly forecast page extends the integrated model through Aug 2028. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Retained-earnings expansion
Estimated revenue	UGX 134,559,220
Estimated production/material cost	UGX 86,324,153
Estimated operating expenses	UGX 15,629,850
Estimated net profit	UGX 32,605,217
Profit target status	Above UGX 20,000,000
Management focus	Test one new district sales route without buying extra machinery.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 33: Sep 2028

This monthly forecast page extends the integrated model through Sep 2028. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Retained-earnings expansion
Estimated revenue	UGX 136,099,440
Estimated production/material cost	UGX 87,312,254
Estimated operating expenses	UGX 15,679,200
Estimated net profit	UGX 33,107,986
Profit target status	Above UGX 20,000,000
Management focus	Review price changes and update the simulator.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 34: Oct 2028

This monthly forecast page extends the integrated model through Oct 2028. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Retained-earnings expansion
Estimated revenue	UGX 137,639,660
Estimated production/material cost	UGX 88,300,356
Estimated operating expenses	UGX 15,728,550
Estimated net profit	UGX 33,610,754
Profit target status	Above UGX 20,000,000
Management focus	Reserve cash for maintenance and pallets.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 35: Nov 2028

This monthly forecast page extends the integrated model through Nov 2028. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Retained-earnings expansion
Estimated revenue	UGX 139,179,880
Estimated production/material cost	UGX 89,288,458
Estimated operating expenses	UGX 15,777,900
Estimated net profit	UGX 34,113,522
Profit target status	Above UGX 20,000,000
Management focus	Prepare quotations for deferred products without committing deposits.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 36: Dec 2028

This monthly forecast page extends the integrated model through Dec 2028. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Retained-earnings expansion
Estimated revenue	UGX 140,720,100
Estimated production/material cost	UGX 90,276,559
Estimated operating expenses	UGX 15,827,250
Estimated net profit	UGX 34,616,291
Profit target status	Above UGX 20,000,000
Management focus	Close the month with inventory count and QC summary.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 37: Jan 2029

This monthly forecast page extends the integrated model through Jan 2029. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Retained-earnings expansion
Estimated revenue	UGX 142,260,320
Estimated production/material cost	UGX 91,264,661
Estimated operating expenses	UGX 15,876,600
Estimated net profit	UGX 35,119,059
Profit target status	Above UGX 20,000,000
Management focus	Verify quotations and protect the UGX 2,000,000 buffer.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 38: Feb 2029

This monthly forecast page extends the integrated model through Feb 2029. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Retained-earnings expansion
Estimated revenue	UGX 143,800,540
Estimated production/material cost	UGX 92,252,763
Estimated operating expenses	UGX 15,925,950
Estimated net profit	UGX 35,621,827
Profit target status	Above UGX 20,000,000
Management focus	Prioritize 6-inch blocks and 8-inch blocks for contractors.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 39: Mar 2029

This monthly forecast page extends the integrated model through Mar 2029. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Retained-earnings expansion
Estimated revenue	UGX 145,340,760
Estimated production/material cost	UGX 93,240,864
Estimated operating expenses	UGX 15,975,300
Estimated net profit	UGX 36,124,596
Profit target status	Above UGX 20,000,000
Management focus	Push 60 mm pavers through schools, homes, and hardware stores.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 40: Apr 2029

This monthly forecast page extends the integrated model through Apr 2029. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Retained-earnings expansion
Estimated revenue	UGX 146,880,980
Estimated production/material cost	UGX 94,228,966
Estimated operating expenses	UGX 16,024,650
Estimated net profit	UGX 36,627,364
Profit target status	Above UGX 20,000,000
Management focus	Use kerbstones only for confirmed contractor orders.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 41: May 2029

This monthly forecast page extends the integrated model through May 2029. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Retained-earnings expansion
Estimated revenue	UGX 148,421,200
Estimated production/material cost	UGX 95,217,068
Estimated operating expenses	UGX 16,074,000
Estimated net profit	UGX 37,130,132
Profit target status	Above UGX 20,000,000
Management focus	Improve curing discipline and reduce rejects.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 42: Jun 2029

This monthly forecast page extends the integrated model through Jun 2029. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Retained-earnings expansion
Estimated revenue	UGX 149,961,420
Estimated production/material cost	UGX 96,205,169
Estimated operating expenses	UGX 16,123,350
Estimated net profit	UGX 37,632,901
Profit target status	Above UGX 20,000,000
Management focus	Collect customer balances before expanding stock.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 43: Jul 2029

This monthly forecast page extends the integrated model through Jul 2029. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Retained-earnings expansion
Estimated revenue	UGX 151,501,640
Estimated production/material cost	UGX 97,193,271
Estimated operating expenses	UGX 16,172,700
Estimated net profit	UGX 38,135,669
Profit target status	Above UGX 20,000,000
Management focus	Negotiate cement distributor terms.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 44: Aug 2029

This monthly forecast page extends the integrated model through Aug 2029. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Retained-earnings expansion
Estimated revenue	UGX 153,041,860
Estimated production/material cost	UGX 98,181,373
Estimated operating expenses	UGX 16,222,050
Estimated net profit	UGX 38,638,437
Profit target status	Above UGX 20,000,000
Management focus	Test one new district sales route without buying extra machinery.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 45: Sep 2029

This monthly forecast page extends the integrated model through Sep 2029. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Retained-earnings expansion
Estimated revenue	UGX 154,582,080
Estimated production/material cost	UGX 99,169,474
Estimated operating expenses	UGX 16,271,400
Estimated net profit	UGX 39,141,206
Profit target status	Above UGX 20,000,000
Management focus	Review price changes and update the simulator.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 46: Oct 2029

This monthly forecast page extends the integrated model through Oct 2029. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Retained-earnings expansion
Estimated revenue	UGX 156,122,300
Estimated production/material cost	UGX 100,157,576
Estimated operating expenses	UGX 16,320,750
Estimated net profit	UGX 39,643,974
Profit target status	Above UGX 20,000,000
Management focus	Reserve cash for maintenance and pallets.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 47: Nov 2029

This monthly forecast page extends the integrated model through Nov 2029. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Retained-earnings expansion
Estimated revenue	UGX 157,662,520
Estimated production/material cost	UGX 101,145,678
Estimated operating expenses	UGX 16,370,100
Estimated net profit	UGX 40,146,742
Profit target status	Above UGX 20,000,000
Management focus	Prepare quotations for deferred products without committing deposits.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 48: Dec 2029

This monthly forecast page extends the integrated model through Dec 2029. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Retained-earnings expansion
Estimated revenue	UGX 159,202,740
Estimated production/material cost	UGX 102,133,779
Estimated operating expenses	UGX 16,419,450
Estimated net profit	UGX 40,649,511
Profit target status	Above UGX 20,000,000
Management focus	Close the month with inventory count and QC summary.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 49: Jan 2030

This monthly forecast page extends the integrated model through Jan 2030. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 171,944,560
Estimated production/material cost	UGX 110,308,075
Estimated operating expenses	UGX 16,468,800
Estimated net profit	UGX 45,167,685
Profit target status	Above UGX 20,000,000
Management focus	Verify quotations and protect the UGX 2,000,000 buffer.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 50: Feb 2030

This monthly forecast page extends the integrated model through Feb 2030. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 173,484,780
Estimated production/material cost	UGX 111,296,176
Estimated operating expenses	UGX 16,518,150
Estimated net profit	UGX 45,670,454
Profit target status	Above UGX 20,000,000
Management focus	Prioritize 6-inch blocks and 8-inch blocks for contractors.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 51: Mar 2030

This monthly forecast page extends the integrated model through Mar 2030. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 175,025,000
Estimated production/material cost	UGX 112,284,278
Estimated operating expenses	UGX 16,567,500
Estimated net profit	UGX 46,173,222
Profit target status	Above UGX 20,000,000
Management focus	Push 60 mm pavers through schools, homes, and hardware stores.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 52: Apr 2030

This monthly forecast page extends the integrated model through Apr 2030. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 176,565,220
Estimated production/material cost	UGX 113,272,380
Estimated operating expenses	UGX 16,616,850
Estimated net profit	UGX 46,675,990
Profit target status	Above UGX 20,000,000
Management focus	Use kerbstones only for confirmed contractor orders.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 53: May 2030

This monthly forecast page extends the integrated model through May 2030. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 178,105,440
Estimated production/material cost	UGX 114,260,481
Estimated operating expenses	UGX 16,666,200
Estimated net profit	UGX 47,178,759
Profit target status	Above UGX 20,000,000
Management focus	Improve curing discipline and reduce rejects.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 54: Jun 2030

This monthly forecast page extends the integrated model through Jun 2030. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 179,645,660
Estimated production/material cost	UGX 115,248,583
Estimated operating expenses	UGX 16,715,550
Estimated net profit	UGX 47,681,527
Profit target status	Above UGX 20,000,000
Management focus	Collect customer balances before expanding stock.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 55: Jul 2030

This monthly forecast page extends the integrated model through Jul 2030. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 181,185,880
Estimated production/material cost	UGX 116,236,684
Estimated operating expenses	UGX 16,764,900
Estimated net profit	UGX 48,184,296
Profit target status	Above UGX 20,000,000
Management focus	Negotiate cement distributor terms.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 56: Aug 2030

This monthly forecast page extends the integrated model through Aug 2030. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 182,726,100
Estimated production/material cost	UGX 117,224,786
Estimated operating expenses	UGX 16,814,250
Estimated net profit	UGX 48,687,064
Profit target status	Above UGX 20,000,000
Management focus	Test one new district sales route without buying extra machinery.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 57: Sep 2030

This monthly forecast page extends the integrated model through Sep 2030. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 184,266,320
Estimated production/material cost	UGX 118,212,888
Estimated operating expenses	UGX 16,863,600
Estimated net profit	UGX 49,189,832
Profit target status	Above UGX 20,000,000
Management focus	Review price changes and update the simulator.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 58: Oct 2030

This monthly forecast page extends the integrated model through Oct 2030. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 185,806,540
Estimated production/material cost	UGX 119,200,989
Estimated operating expenses	UGX 16,912,950
Estimated net profit	UGX 49,692,601
Profit target status	Above UGX 20,000,000
Management focus	Reserve cash for maintenance and pallets.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 59: Nov 2030

This monthly forecast page extends the integrated model through Nov 2030. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 187,346,760
Estimated production/material cost	UGX 120,189,091
Estimated operating expenses	UGX 16,962,300
Estimated net profit	UGX 50,195,369
Profit target status	Above UGX 20,000,000
Management focus	Prepare quotations for deferred products without committing deposits.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 60: Dec 2030

This monthly forecast page extends the integrated model through Dec 2030. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 188,886,980
Estimated production/material cost	UGX 121,177,193
Estimated operating expenses	UGX 17,011,650
Estimated net profit	UGX 50,698,137
Profit target status	Above UGX 20,000,000
Management focus	Close the month with inventory count and QC summary.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 61: Jan 2031

This monthly forecast page extends the integrated model through Jan 2031. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 190,427,200
Estimated production/material cost	UGX 122,165,294
Estimated operating expenses	UGX 17,061,000
Estimated net profit	UGX 51,200,906
Profit target status	Above UGX 20,000,000
Management focus	Verify quotations and protect the UGX 2,000,000 buffer.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 62: Feb 2031

This monthly forecast page extends the integrated model through Feb 2031. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 191,967,420
Estimated production/material cost	UGX 123,153,396
Estimated operating expenses	UGX 17,110,350
Estimated net profit	UGX 51,703,674
Profit target status	Above UGX 20,000,000
Management focus	Prioritize 6-inch blocks and 8-inch blocks for contractors.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 63: Mar 2031

This monthly forecast page extends the integrated model through Mar 2031. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 193,507,640
Estimated production/material cost	UGX 124,141,498
Estimated operating expenses	UGX 17,159,700
Estimated net profit	UGX 52,206,442
Profit target status	Above UGX 20,000,000
Management focus	Push 60 mm pavers through schools, homes, and hardware stores.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 64: Apr 2031

This monthly forecast page extends the integrated model through Apr 2031. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 195,047,860
Estimated production/material cost	UGX 125,129,599
Estimated operating expenses	UGX 17,209,050
Estimated net profit	UGX 52,709,211
Profit target status	Above UGX 20,000,000
Management focus	Use kerbstones only for confirmed contractor orders.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 65: May 2031

This monthly forecast page extends the integrated model through May 2031. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 196,588,080
Estimated production/material cost	UGX 126,117,701
Estimated operating expenses	UGX 17,258,400
Estimated net profit	UGX 53,211,979
Profit target status	Above UGX 20,000,000
Management focus	Improve curing discipline and reduce rejects.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 66: Jun 2031

This monthly forecast page extends the integrated model through Jun 2031. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 198,128,300
Estimated production/material cost	UGX 127,105,803
Estimated operating expenses	UGX 17,307,750
Estimated net profit	UGX 53,714,747
Profit target status	Above UGX 20,000,000
Management focus	Collect customer balances before expanding stock.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 67: Jul 2031

This monthly forecast page extends the integrated model through Jul 2031. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 199,668,520
Estimated production/material cost	UGX 128,093,904
Estimated operating expenses	UGX 17,357,100
Estimated net profit	UGX 54,217,516
Profit target status	Above UGX 20,000,000
Management focus	Negotiate cement distributor terms.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 68: Aug 2031

This monthly forecast page extends the integrated model through Aug 2031. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 201,208,740
Estimated production/material cost	UGX 129,082,006
Estimated operating expenses	UGX 17,406,450
Estimated net profit	UGX 54,720,284
Profit target status	Above UGX 20,000,000
Management focus	Test one new district sales route without buying extra machinery.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 69: Sep 2031

This monthly forecast page extends the integrated model through Sep 2031. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 202,748,960
Estimated production/material cost	UGX 130,070,107
Estimated operating expenses	UGX 17,455,800
Estimated net profit	UGX 55,223,053
Profit target status	Above UGX 20,000,000
Management focus	Review price changes and update the simulator.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 70: Oct 2031

This monthly forecast page extends the integrated model through Oct 2031. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 204,289,180
Estimated production/material cost	UGX 131,058,209
Estimated operating expenses	UGX 17,505,150
Estimated net profit	UGX 55,725,821
Profit target status	Above UGX 20,000,000
Management focus	Reserve cash for maintenance and pallets.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 71: Nov 2031

This monthly forecast page extends the integrated model through Nov 2031. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 205,829,400
Estimated production/material cost	UGX 132,046,311
Estimated operating expenses	UGX 17,554,500
Estimated net profit	UGX 56,228,589
Profit target status	Above UGX 20,000,000
Management focus	Prepare quotations for deferred products without committing deposits.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 72: Dec 2031

This monthly forecast page extends the integrated model through Dec 2031. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 207,369,620
Estimated production/material cost	UGX 133,034,412
Estimated operating expenses	UGX 17,603,850
Estimated net profit	UGX 56,731,358
Profit target status	Above UGX 20,000,000
Management focus	Close the month with inventory count and QC summary.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 73: Jan 2032

This monthly forecast page extends the integrated model through Jan 2032. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 208,909,840
Estimated production/material cost	UGX 134,022,514
Estimated operating expenses	UGX 17,653,200
Estimated net profit	UGX 57,234,126
Profit target status	Above UGX 20,000,000
Management focus	Verify quotations and protect the UGX 2,000,000 buffer.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 74: Feb 2032

This monthly forecast page extends the integrated model through Feb 2032. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 210,450,060
Estimated production/material cost	UGX 135,010,616
Estimated operating expenses	UGX 17,702,550
Estimated net profit	UGX 57,736,894
Profit target status	Above UGX 20,000,000
Management focus	Prioritize 6-inch blocks and 8-inch blocks for contractors.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 75: Mar 2032

This monthly forecast page extends the integrated model through Mar 2032. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 211,990,280
Estimated production/material cost	UGX 135,998,717
Estimated operating expenses	UGX 17,751,900
Estimated net profit	UGX 58,239,663
Profit target status	Above UGX 20,000,000
Management focus	Push 60 mm pavers through schools, homes, and hardware stores.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 76: Apr 2032

This monthly forecast page extends the integrated model through Apr 2032. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 213,530,500
Estimated production/material cost	UGX 136,986,819
Estimated operating expenses	UGX 17,801,250
Estimated net profit	UGX 58,742,431
Profit target status	Above UGX 20,000,000
Management focus	Use kerbstones only for confirmed contractor orders.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 77: May 2032

This monthly forecast page extends the integrated model through May 2032. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 215,070,720
Estimated production/material cost	UGX 137,974,921
Estimated operating expenses	UGX 17,850,600
Estimated net profit	UGX 59,245,199
Profit target status	Above UGX 20,000,000
Management focus	Improve curing discipline and reduce rejects.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 78: Jun 2032

This monthly forecast page extends the integrated model through Jun 2032. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 216,610,940
Estimated production/material cost	UGX 138,963,022
Estimated operating expenses	UGX 17,899,950
Estimated net profit	UGX 59,747,968
Profit target status	Above UGX 20,000,000
Management focus	Collect customer balances before expanding stock.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 79: Jul 2032

This monthly forecast page extends the integrated model through Jul 2032. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 218,151,160
Estimated production/material cost	UGX 139,951,124
Estimated operating expenses	UGX 17,949,300
Estimated net profit	UGX 60,250,736
Profit target status	Above UGX 20,000,000
Management focus	Negotiate cement distributor terms.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 80: Aug 2032

This monthly forecast page extends the integrated model through Aug 2032. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 219,691,380
Estimated production/material cost	UGX 140,939,226
Estimated operating expenses	UGX 17,998,650
Estimated net profit	UGX 60,753,504
Profit target status	Above UGX 20,000,000
Management focus	Test one new district sales route without buying extra machinery.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 81: Sep 2032

This monthly forecast page extends the integrated model through Sep 2032. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 221,231,600
Estimated production/material cost	UGX 141,927,327
Estimated operating expenses	UGX 18,048,000
Estimated net profit	UGX 61,256,273
Profit target status	Above UGX 20,000,000
Management focus	Review price changes and update the simulator.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 82: Oct 2032

This monthly forecast page extends the integrated model through Oct 2032. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 222,771,820
Estimated production/material cost	UGX 142,915,429
Estimated operating expenses	UGX 18,097,350
Estimated net profit	UGX 61,759,041
Profit target status	Above UGX 20,000,000
Management focus	Reserve cash for maintenance and pallets.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 83: Nov 2032

This monthly forecast page extends the integrated model through Nov 2032. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 224,312,040
Estimated production/material cost	UGX 143,903,531
Estimated operating expenses	UGX 18,146,700
Estimated net profit	UGX 62,261,809
Profit target status	Above UGX 20,000,000
Management focus	Prepare quotations for deferred products without committing deposits.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 84: Dec 2032

This monthly forecast page extends the integrated model through Dec 2032. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 225,852,260
Estimated production/material cost	UGX 144,891,632
Estimated operating expenses	UGX 18,196,050
Estimated net profit	UGX 62,764,578
Profit target status	Above UGX 20,000,000
Management focus	Close the month with inventory count and QC summary.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 85: Jan 2033

This monthly forecast page extends the integrated model through Jan 2033. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 227,392,480
Estimated production/material cost	UGX 145,879,734
Estimated operating expenses	UGX 18,245,400
Estimated net profit	UGX 63,267,346
Profit target status	Above UGX 20,000,000
Management focus	Verify quotations and protect the UGX 2,000,000 buffer.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 86: Feb 2033

This monthly forecast page extends the integrated model through Feb 2033. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 228,932,700
Estimated production/material cost	UGX 146,867,835
Estimated operating expenses	UGX 18,294,750
Estimated net profit	UGX 63,770,115
Profit target status	Above UGX 20,000,000
Management focus	Prioritize 6-inch blocks and 8-inch blocks for contractors.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 87: Mar 2033

This monthly forecast page extends the integrated model through Mar 2033. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 230,472,920
Estimated production/material cost	UGX 147,855,937
Estimated operating expenses	UGX 18,344,100
Estimated net profit	UGX 64,272,883
Profit target status	Above UGX 20,000,000
Management focus	Push 60 mm pavers through schools, homes, and hardware stores.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 88: Apr 2033

This monthly forecast page extends the integrated model through Apr 2033. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 232,013,140
Estimated production/material cost	UGX 148,844,039
Estimated operating expenses	UGX 18,393,450
Estimated net profit	UGX 64,775,651
Profit target status	Above UGX 20,000,000
Management focus	Use kerbstones only for confirmed contractor orders.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 89: May 2033

This monthly forecast page extends the integrated model through May 2033. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 233,553,360
Estimated production/material cost	UGX 149,832,140
Estimated operating expenses	UGX 18,442,800
Estimated net profit	UGX 65,278,420
Profit target status	Above UGX 20,000,000
Management focus	Improve curing discipline and reduce rejects.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 90: Jun 2033

This monthly forecast page extends the integrated model through Jun 2033. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 235,093,580
Estimated production/material cost	UGX 150,820,242
Estimated operating expenses	UGX 18,492,150
Estimated net profit	UGX 65,781,188
Profit target status	Above UGX 20,000,000
Management focus	Collect customer balances before expanding stock.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 91: Jul 2033

This monthly forecast page extends the integrated model through Jul 2033. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 236,633,800
Estimated production/material cost	UGX 151,808,344
Estimated operating expenses	UGX 18,541,500
Estimated net profit	UGX 66,283,956
Profit target status	Above UGX 20,000,000
Management focus	Negotiate cement distributor terms.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 92: Aug 2033

This monthly forecast page extends the integrated model through Aug 2033. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 238,174,020
Estimated production/material cost	UGX 152,796,445
Estimated operating expenses	UGX 18,590,850
Estimated net profit	UGX 66,786,725
Profit target status	Above UGX 20,000,000
Management focus	Test one new district sales route without buying extra machinery.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 93: Sep 2033

This monthly forecast page extends the integrated model through Sep 2033. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 239,714,240
Estimated production/material cost	UGX 153,784,547
Estimated operating expenses	UGX 18,640,200
Estimated net profit	UGX 67,289,493
Profit target status	Above UGX 20,000,000
Management focus	Review price changes and update the simulator.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 94: Oct 2033

This monthly forecast page extends the integrated model through Oct 2033. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 241,254,460
Estimated production/material cost	UGX 154,772,649
Estimated operating expenses	UGX 18,689,550
Estimated net profit	UGX 67,792,261
Profit target status	Above UGX 20,000,000
Management focus	Reserve cash for maintenance and pallets.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 95: Nov 2033

This monthly forecast page extends the integrated model through Nov 2033. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 242,794,680
Estimated production/material cost	UGX 155,760,750
Estimated operating expenses	UGX 18,738,900
Estimated net profit	UGX 68,295,030
Profit target status	Above UGX 20,000,000
Management focus	Prepare quotations for deferred products without committing deposits.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 96: Dec 2033

This monthly forecast page extends the integrated model through Dec 2033. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 244,334,900
Estimated production/material cost	UGX 156,748,852
Estimated operating expenses	UGX 18,788,250
Estimated net profit	UGX 68,797,798
Profit target status	Above UGX 20,000,000
Management focus	Close the month with inventory count and QC summary.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 97: Jan 2034

This monthly forecast page extends the integrated model through Jan 2034. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 245,875,120
Estimated production/material cost	UGX 157,736,954
Estimated operating expenses	UGX 18,837,600
Estimated net profit	UGX 69,300,566
Profit target status	Above UGX 20,000,000
Management focus	Verify quotations and protect the UGX 2,000,000 buffer.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 98: Feb 2034

This monthly forecast page extends the integrated model through Feb 2034. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 247,415,340
Estimated production/material cost	UGX 158,725,055
Estimated operating expenses	UGX 18,886,950
Estimated net profit	UGX 69,803,335
Profit target status	Above UGX 20,000,000
Management focus	Prioritize 6-inch blocks and 8-inch blocks for contractors.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 99: Mar 2034

This monthly forecast page extends the integrated model through Mar 2034. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 248,955,560
Estimated production/material cost	UGX 159,713,157
Estimated operating expenses	UGX 18,936,300
Estimated net profit	UGX 70,306,103
Profit target status	Above UGX 20,000,000
Management focus	Push 60 mm pavers through schools, homes, and hardware stores.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 100: Apr 2034

This monthly forecast page extends the integrated model through Apr 2034. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 250,495,780
Estimated production/material cost	UGX 160,701,258
Estimated operating expenses	UGX 18,985,650
Estimated net profit	UGX 70,808,872
Profit target status	Above UGX 20,000,000
Management focus	Use kerbstones only for confirmed contractor orders.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 101: May 2034

This monthly forecast page extends the integrated model through May 2034. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 252,036,000
Estimated production/material cost	UGX 161,689,360
Estimated operating expenses	UGX 19,035,000
Estimated net profit	UGX 71,311,640
Profit target status	Above UGX 20,000,000
Management focus	Improve curing discipline and reduce rejects.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 102: Jun 2034

This monthly forecast page extends the integrated model through Jun 2034. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 253,576,220
Estimated production/material cost	UGX 162,677,462
Estimated operating expenses	UGX 19,084,350
Estimated net profit	UGX 71,814,408
Profit target status	Above UGX 20,000,000
Management focus	Collect customer balances before expanding stock.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 103: Jul 2034

This monthly forecast page extends the integrated model through Jul 2034. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 255,116,440
Estimated production/material cost	UGX 163,665,563
Estimated operating expenses	UGX 19,133,700
Estimated net profit	UGX 72,317,177
Profit target status	Above UGX 20,000,000
Management focus	Negotiate cement distributor terms.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 104: Aug 2034

This monthly forecast page extends the integrated model through Aug 2034. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 256,656,660
Estimated production/material cost	UGX 164,653,665
Estimated operating expenses	UGX 19,183,050
Estimated net profit	UGX 72,819,945
Profit target status	Above UGX 20,000,000
Management focus	Test one new district sales route without buying extra machinery.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 105: Sep 2034

This monthly forecast page extends the integrated model through Sep 2034. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 258,196,880
Estimated production/material cost	UGX 165,641,767
Estimated operating expenses	UGX 19,232,400
Estimated net profit	UGX 73,322,713
Profit target status	Above UGX 20,000,000
Management focus	Review price changes and update the simulator.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 106: Oct 2034

This monthly forecast page extends the integrated model through Oct 2034. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 259,737,100
Estimated production/material cost	UGX 166,629,868
Estimated operating expenses	UGX 19,281,750
Estimated net profit	UGX 73,825,482
Profit target status	Above UGX 20,000,000
Management focus	Reserve cash for maintenance and pallets.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 107: Nov 2034

This monthly forecast page extends the integrated model through Nov 2034. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 261,277,320
Estimated production/material cost	UGX 167,617,970
Estimated operating expenses	UGX 19,331,100
Estimated net profit	UGX 74,328,250
Profit target status	Above UGX 20,000,000
Management focus	Prepare quotations for deferred products without committing deposits.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 108: Dec 2034

This monthly forecast page extends the integrated model through Dec 2034. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 262,817,540
Estimated production/material cost	UGX 168,606,072
Estimated operating expenses	UGX 19,380,450
Estimated net profit	UGX 74,831,018
Profit target status	Above UGX 20,000,000
Management focus	Close the month with inventory count and QC summary.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 109: Jan 2035

This monthly forecast page extends the integrated model through Jan 2035. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 264,357,760
Estimated production/material cost	UGX 169,594,173
Estimated operating expenses	UGX 19,429,800
Estimated net profit	UGX 75,333,787
Profit target status	Above UGX 20,000,000
Management focus	Verify quotations and protect the UGX 2,000,000 buffer.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 110: Feb 2035

This monthly forecast page extends the integrated model through Feb 2035. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 265,897,980
Estimated production/material cost	UGX 170,582,275
Estimated operating expenses	UGX 19,479,150
Estimated net profit	UGX 75,836,555
Profit target status	Above UGX 20,000,000
Management focus	Prioritize 6-inch blocks and 8-inch blocks for contractors.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 111: Mar 2035

This monthly forecast page extends the integrated model through Mar 2035. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 267,438,200
Estimated production/material cost	UGX 171,570,377
Estimated operating expenses	UGX 19,528,500
Estimated net profit	UGX 76,339,323
Profit target status	Above UGX 20,000,000
Management focus	Push 60 mm pavers through schools, homes, and hardware stores.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 112: Apr 2035

This monthly forecast page extends the integrated model through Apr 2035. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 268,978,420
Estimated production/material cost	UGX 172,558,478
Estimated operating expenses	UGX 19,577,850
Estimated net profit	UGX 76,842,092
Profit target status	Above UGX 20,000,000
Management focus	Use kerbstones only for confirmed contractor orders.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 113: May 2035

This monthly forecast page extends the integrated model through May 2035. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 270,518,640
Estimated production/material cost	UGX 173,546,580
Estimated operating expenses	UGX 19,627,200
Estimated net profit	UGX 77,344,860
Profit target status	Above UGX 20,000,000
Management focus	Improve curing discipline and reduce rejects.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 114: Jun 2035

This monthly forecast page extends the integrated model through Jun 2035. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 272,058,860
Estimated production/material cost	UGX 174,534,682
Estimated operating expenses	UGX 19,676,550
Estimated net profit	UGX 77,847,628
Profit target status	Above UGX 20,000,000
Management focus	Collect customer balances before expanding stock.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 115: Jul 2035

This monthly forecast page extends the integrated model through Jul 2035. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 273,599,080
Estimated production/material cost	UGX 175,522,783
Estimated operating expenses	UGX 19,725,900
Estimated net profit	UGX 78,350,397
Profit target status	Above UGX 20,000,000
Management focus	Negotiate cement distributor terms.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 116: Aug 2035

This monthly forecast page extends the integrated model through Aug 2035. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 275,139,300
Estimated production/material cost	UGX 176,510,885
Estimated operating expenses	UGX 19,775,250
Estimated net profit	UGX 78,853,165
Profit target status	Above UGX 20,000,000
Management focus	Test one new district sales route without buying extra machinery.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 117: Sep 2035

This monthly forecast page extends the integrated model through Sep 2035. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 276,679,520
Estimated production/material cost	UGX 177,498,986
Estimated operating expenses	UGX 19,824,600
Estimated net profit	UGX 79,355,934
Profit target status	Above UGX 20,000,000
Management focus	Review price changes and update the simulator.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 118: Oct 2035

This monthly forecast page extends the integrated model through Oct 2035. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 278,219,740
Estimated production/material cost	UGX 178,487,088
Estimated operating expenses	UGX 19,873,950
Estimated net profit	UGX 79,858,702
Profit target status	Above UGX 20,000,000
Management focus	Reserve cash for maintenance and pallets.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 119: Nov 2035

This monthly forecast page extends the integrated model through Nov 2035. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 279,759,960
Estimated production/material cost	UGX 179,475,190
Estimated operating expenses	UGX 19,923,300
Estimated net profit	UGX 80,361,470
Profit target status	Above UGX 20,000,000
Management focus	Prepare quotations for deferred products without committing deposits.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix Monthly Forecast 120: Dec 2035

This monthly forecast page extends the integrated model through Dec 2035. It remains an estimated planning view, not an audited projection. The operating discipline is to keep the original UGX 130,000,000 launch scope intact until cash flow and verified demand justify expansion.

Planning phase	Expansion evaluation
Estimated revenue	UGX 281,300,180
Estimated production/material cost	UGX 180,463,291
Estimated operating expenses	UGX 19,972,650
Estimated net profit	UGX 80,864,239
Profit target status	Above UGX 20,000,000
Management focus	Close the month with inventory count and QC summary.
Data confidence	Estimated; update with actual sales, stock counts, supplier invoices, and QC results.

Appendix District Sales Campaign 1: Mbarara City

Mbarara City is part of the Western Uganda launch map. The sales campaign should begin with direct contractor visits, hardware store checks, school and institutional project tracking, and phone-based quotation requests. No route should receive permanent stock until demand and payment reliability are observed.

Primary products	6-inch hollow blocks, 8-inch hollow blocks, 60 mm pavers, 80 mm pavers, kerbstones where confirmed
Deferred products	Ready-mix concrete, culverts, drainage channels, grass pavers, cobblestones
Price discipline	Quote in UGX only and compare against verified local competitor prices.
Credit discipline	Use deposits for delivery-heavy orders and track customer balances in the ERP module.
Operational check	Confirm transport cost, delivery radius, road access, and unloading method before accepting orders.
Data confidence	Needs field verification before investment decisions.

Appendix District Sales Campaign 2: Rwampara

Rwampara is part of the Western Uganda launch map. The sales campaign should begin with direct contractor visits, hardware store checks, school and institutional project tracking, and phone-based quotation requests. No route should receive permanent stock until demand and payment reliability are observed.

Primary products	6-inch hollow blocks, 8-inch hollow blocks, 60 mm pavers, 80 mm pavers, kerbstones where confirmed
Deferred products	Ready-mix concrete, culverts, drainage channels, grass pavers, cobblestones
Price discipline	Quote in UGX only and compare against verified local competitor prices.
Credit discipline	Use deposits for delivery-heavy orders and track customer balances in the ERP module.
Operational check	Confirm transport cost, delivery radius, road access, and unloading method before accepting orders.
Data confidence	Needs field verification before investment decisions.

Appendix District Sales Campaign 3: Isingiro

Isingiro is part of the Western Uganda launch map. The sales campaign should begin with direct contractor visits, hardware store checks, school and institutional project tracking, and phone-based quotation requests. No route should receive permanent stock until demand and payment reliability are observed.

Primary products	6-inch hollow blocks, 8-inch hollow blocks, 60 mm pavers, 80 mm pavers, kerbstones where confirmed
Deferred products	Ready-mix concrete, culverts, drainage channels, grass pavers, cobblestones
Price discipline	Quote in UGX only and compare against verified local competitor prices.
Credit discipline	Use deposits for delivery-heavy orders and track customer balances in the ERP module.
Operational check	Confirm transport cost, delivery radius, road access, and unloading method before accepting orders.
Data confidence	Needs field verification before investment decisions.

Appendix District Sales Campaign 4: Ntungamo

Ntungamo is part of the Western Uganda launch map. The sales campaign should begin with direct contractor visits, hardware store checks, school and institutional project tracking, and phone-based quotation requests. No route should receive permanent stock until demand and payment reliability are observed.

Primary products	6-inch hollow blocks, 8-inch hollow blocks, 60 mm pavers, 80 mm pavers, kerbstones where confirmed
Deferred products	Ready-mix concrete, culverts, drainage channels, grass pavers, cobblestones
Price discipline	Quote in UGX only and compare against verified local competitor prices.
Credit discipline	Use deposits for delivery-heavy orders and track customer balances in the ERP module.
Operational check	Confirm transport cost, delivery radius, road access, and unloading method before accepting orders.
Data confidence	Needs field verification before investment decisions.

Appendix District Sales Campaign 5: Bushenyi

Bushenyi is part of the Western Uganda launch map. The sales campaign should begin with direct contractor visits, hardware store checks, school and institutional project tracking, and phone-based quotation requests. No route should receive permanent stock until demand and payment reliability are observed.

Primary products	6-inch hollow blocks, 8-inch hollow blocks, 60 mm pavers, 80 mm pavers, kerbstones where confirmed
Deferred products	Ready-mix concrete, culverts, drainage channels, grass pavers, cobblestones
Price discipline	Quote in UGX only and compare against verified local competitor prices.
Credit discipline	Use deposits for delivery-heavy orders and track customer balances in the ERP module.
Operational check	Confirm transport cost, delivery radius, road access, and unloading method before accepting orders.
Data confidence	Needs field verification before investment decisions.

Appendix District Sales Campaign 6: Ibanda

Ibanda is part of the Western Uganda launch map. The sales campaign should begin with direct contractor visits, hardware store checks, school and institutional project tracking, and phone-based quotation requests. No route should receive permanent stock until demand and payment reliability are observed.

Primary products	6-inch hollow blocks, 8-inch hollow blocks, 60 mm pavers, 80 mm pavers, kerbstones where confirmed
Deferred products	Ready-mix concrete, culverts, drainage channels, grass pavers, cobblestones
Price discipline	Quote in UGX only and compare against verified local competitor prices.
Credit discipline	Use deposits for delivery-heavy orders and track customer balances in the ERP module.
Operational check	Confirm transport cost, delivery radius, road access, and unloading method before accepting orders.
Data confidence	Needs field verification before investment decisions.

Appendix District Sales Campaign 7: Kiruhura

Kiruhura is part of the Western Uganda launch map. The sales campaign should begin with direct contractor visits, hardware store checks, school and institutional project tracking, and phone-based quotation requests. No route should receive permanent stock until demand and payment reliability are observed.

Primary products	6-inch hollow blocks, 8-inch hollow blocks, 60 mm pavers, 80 mm pavers, kerbstones where confirmed
Deferred products	Ready-mix concrete, culverts, drainage channels, grass pavers, cobblestones
Price discipline	Quote in UGX only and compare against verified local competitor prices.
Credit discipline	Use deposits for delivery-heavy orders and track customer balances in the ERP module.
Operational check	Confirm transport cost, delivery radius, road access, and unloading method before accepting orders.
Data confidence	Needs field verification before investment decisions.

Appendix District Sales Campaign 8: Sheema

Sheema is part of the Western Uganda launch map. The sales campaign should begin with direct contractor visits, hardware store checks, school and institutional project tracking, and phone-based quotation requests. No route should receive permanent stock until demand and payment reliability are observed.

Primary products	6-inch hollow blocks, 8-inch hollow blocks, 60 mm pavers, 80 mm pavers, kerbstones where confirmed
Deferred products	Ready-mix concrete, culverts, drainage channels, grass pavers, cobblestones
Price discipline	Quote in UGX only and compare against verified local competitor prices.
Credit discipline	Use deposits for delivery-heavy orders and track customer balances in the ERP module.
Operational check	Confirm transport cost, delivery radius, road access, and unloading method before accepting orders.
Data confidence	Needs field verification before investment decisions.

Appendix District Sales Campaign 9: Lyantonde

Lyantonde is part of the Western Uganda launch map. The sales campaign should begin with direct contractor visits, hardware store checks, school and institutional project tracking, and phone-based quotation requests. No route should receive permanent stock until demand and payment reliability are observed.

Primary products	6-inch hollow blocks, 8-inch hollow blocks, 60 mm pavers, 80 mm pavers, kerbstones where confirmed
Deferred products	Ready-mix concrete, culverts, drainage channels, grass pavers, cobblestones
Price discipline	Quote in UGX only and compare against verified local competitor prices.
Credit discipline	Use deposits for delivery-heavy orders and track customer balances in the ERP module.
Operational check	Confirm transport cost, delivery radius, road access, and unloading method before accepting orders.
Data confidence	Needs field verification before investment decisions.

Appendix District Sales Campaign 10: Kabale

Kabale is part of the Western Uganda launch map. The sales campaign should begin with direct contractor visits, hardware store checks, school and institutional project tracking, and phone-based quotation requests. No route should receive permanent stock until demand and payment reliability are observed.

Primary products	6-inch hollow blocks, 8-inch hollow blocks, 60 mm pavers, 80 mm pavers, kerbstones where confirmed
Deferred products	Ready-mix concrete, culverts, drainage channels, grass pavers, cobblestones
Price discipline	Quote in UGX only and compare against verified local competitor prices.
Credit discipline	Use deposits for delivery-heavy orders and track customer balances in the ERP module.
Operational check	Confirm transport cost, delivery radius, road access, and unloading method before accepting orders.
Data confidence	Needs field verification before investment decisions.

Appendix District Sales Campaign 11: Rukungiri

Rukungiri is part of the Western Uganda launch map. The sales campaign should begin with direct contractor visits, hardware store checks, school and institutional project tracking, and phone-based quotation requests. No route should receive permanent stock until demand and payment reliability are observed.

Primary products	6-inch hollow blocks, 8-inch hollow blocks, 60 mm pavers, 80 mm pavers, kerbstones where confirmed
Deferred products	Ready-mix concrete, culverts, drainage channels, grass pavers, cobblestones
Price discipline	Quote in UGX only and compare against verified local competitor prices.
Credit discipline	Use deposits for delivery-heavy orders and track customer balances in the ERP module.
Operational check	Confirm transport cost, delivery radius, road access, and unloading method before accepting orders.
Data confidence	Needs field verification before investment decisions.
